

FIELD INSPECTION REPORT

Project Name:	Mountain Valley Pipeline	Inspector: M. Willis	Matthew Grant
Inspection Date:	Monday, March 17, 2025	Project Contact:	Brian Clauto Cory Chalmers
Spread G: Giles	Sta 10820-10860 GI 241.03	Weather:	Dry

ACTIVE STAGE OF CONSTRUCTION: (Check all that apply)

- ☐ Tree Felling
 ☐ Clearing/Grubbing
 ☐ Grading
 ☐ Trenching
 ☐ Stringing/Welding
☐ Lowering/Backfilling
 ☐ Final Grading
 ☐ Temp. Stabilization
 ☒ Perm. Stabilization
 ☐ Other

- | | | Yes | No | N/A |
|----|---|-------------------------------------|-------------------------------------|--------------------------|
| 1. | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |
| 2. | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | <input type="checkbox"/> |
| 3. | Areas of offsite sediment deposition observed? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | <input type="checkbox"/> |

▪ Comments: Designated Stream S-YZ1, S-A34, S-A33 were inspected ESC remains in place.

Routine Maintenance: (72-Hour Deadline from Notification)

- STA10820-10826, requires re stabilization.
- STA 10830-10831 requires re stabilization.
- STA10840-10846 requires re stabilization and rill erosion repair.
- STA 10850 permanent waterbar requires cleanout and re stabilization.


Ineffective Controls: (24-Hour Deadline from Notification)

- N/A.

Recommended Corrective Action: Maintain and install all controls per the approved PSS&S.

Deadline: Within 72-Hour of Notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.

Inspector Signature: _____  _____

Date: Monday, March 17, 2025

FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Monday, March 17, 2025

Figure 1: STA 10823, re stabilization is required on denuded areas.



Figure 2: STA 10830, re stabilization is required on denuded areas.

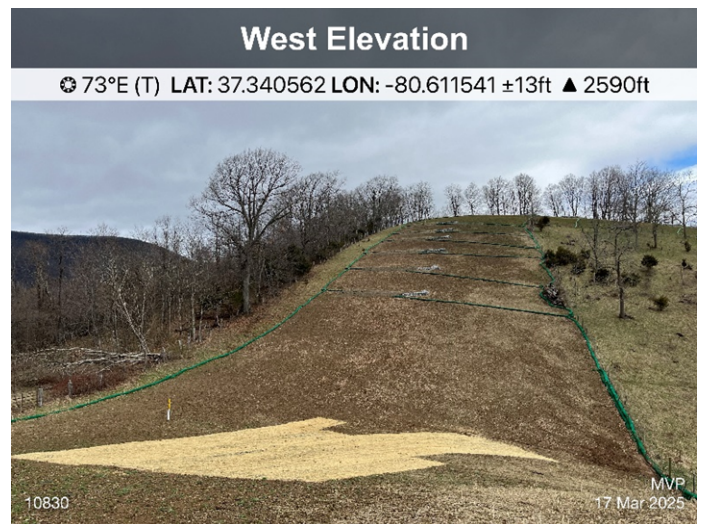


Figure 3: STA 10843, re stabilization is required on denuded areas.

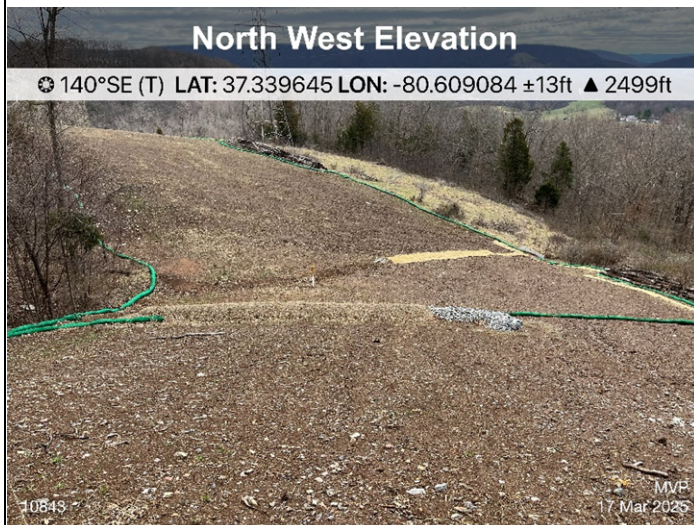


Figure 4: STA 10850, permanent waterbar requires cleanout and re stabilization.

