

FIELD INSPECTION

Project Name:	Mountain Valley Pipeline	Inspector:	Matthew Grant
Inspection Date:	Thursday, September 5, 2019	Project Contact:	Brian Clauto
Spread: Roanoke Co. MP246.5-246.7 Franklin Co. MP248 MP251 MP252	Spread H	Weather (Wet/Dry/Rain):	Dry

STAGE OF CONSTRUCTION: (Check all that apply)

- ☐ Clearing
 ☐ Rough Grading
 ☐ Trench Excavation
 ☐ Pipe Assembly, Testing & Installation
☒ Backfilling and Grade Restoration
 ☒ Final Grading & Stabilization
 ☒ Other: Bore site/ Dormant

- | | | Yes | No | N/A |
|---|---|-------------------------------------|-------------------------------------|--------------------------|
| 1 | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | ☒ | ☐ | ☐ |
| 2 | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | ☐ | ☒ | ☐ |
| 3 | Areas of offsite sediment deposition were observed? | ☐ | ☒ | ☐ |

Comments:

- Inspected designated streams included: SH-1, W-EF3, S-II4, GH-7
- ECD's were in place for active construction and functioning at designated stream & wetland crossings.
- Near ST13308+99 the stock pile lacks stabilization

Recommend Corrective Action: Maintain and install all controls per the approved plan and specs

Deadline: Within 24hr notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.


Inspector Signature: Matthew Grant Date: 10-9-19

FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Thursday, September 5, 2019

- Fig. 1 Active bore site near GH-7

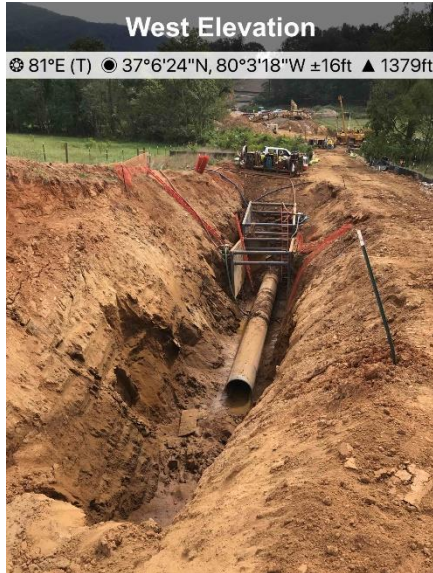

- Fig. 2. Active bore site near GH-7, stockpile near ST13308+99 lacks stabilization.



- Fig. 3 Near MP 246.7 stabilization and permanent bars have been installed.



- Fig. 4 Near St13098+00 ongoing grading

