

FIELD INSPECTION

Project Name:	Mountain Valley Pipeline	Inspector:	Matthew Grant
Inspection Date:	Tuesday, October 16, 2018	Project Contact:	Brian Clauto
Spread: Franklin County MP 263 St#130903-13938	Spread I	Weather (Wet/Dry/Rain):	Wet

STAGE OF CONSTRUCTION: (Check all that apply)

- ☐ Clearing

☐ Rough Grading

☐ Trench Excavation

☐ Pipe Assembly, Testing & Installation

☐ Backfilling and Grade Restoration

☐ Final Grading & Stabilization

☒ Other: E&S repair

- | | | Yes | No | N/A |
|---|---|-------------------------------------|--------------------------|--------------------------|
| 1 | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | ☒ | ☐ | ☐ |
| 2 | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | ☒ | ☐ | ☐ |
| 3 | Areas of offsite sediment deposition were observed? | ☒ | ☐ | ☐ |

Comments:

- **Area 1** –MP 263 St#13903-13938 Observations: no work was being conducted in the wetlands or streams within this area per the Nationwide Permit 12 Verification Suspension letter dated 10/5/18. The area between St#13903 and St#13926 lacks stabilization, at St#13903+00 sediment has left the ROW. At St#13916+23 debris is outside of ROW, which had been noted in the SWPPP by MVP.

Recommended Corrective Action: Stabilized slope between stations 13903 and 13926 and remove sediment per DEQ approval.

Deadline: Within 24 hr notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.

Inspector Signature: Matthew Grant Date: 11-5-18

FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Tuesday, October 16, 2018

Fig. 1
The area between 13903 and St#13926 lacks stabilization.

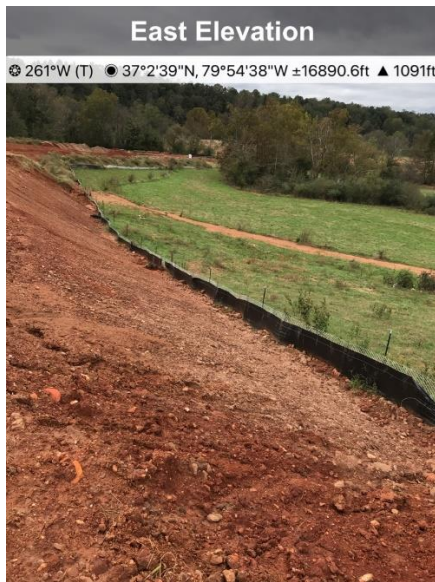


Fig. 2
At St#13903+00 sediment has left the ROW.



Fig. 3.
At St#13916+23 debris is outside of ROW.



Fig 4.
Designated stream SII2

