

FIELD INSPECTION

Project Name:	Mountain Valley Pipeline	Inspector:	Matthew Grant
Inspection Date:	Wednesday, March 20, 2019	Project Contact:	Brian Clauto
Spread: Franklin County MP256-255 St1347-13496 MP261 St13818-13805	Spread I	Weather (Wet/Dry/Rain):	Dry

STAGE OF CONSTRUCTION: (Check all that apply)

- ☐ Clearing

☐ Rough Grading

☐ Trench Excavation

☐ Pipe Assembly, Testing & Installation

☐ Backfilling and Grade Restoration

☒ Final Grading & Stabilization

☒ Other: Dormant

- | | | Yes | No | N/A |
|---|---|-------------------------------------|-------------------------------------|--------------------------|
| 1 | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | ☒ | ☐ | ☐ |
| 2 | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | ☐ | ☒ | ☐ |
| 3 | Areas of offsite sediment deposition were observed? | ☐ | ☒ | ☐ |


Comments:

- Streams / wetlands inspected included: II-7, II-8, W-IJ6
- St#13539+14 Slope lacks adequate stabilization
- St#13533+52 Banks require repair and stabilization
- St#13528+00 Rills at former road crossing and CFS requires maintenance
- St#13500+00 Rill erosion along P1 SF and J-hook is overtopped
- St#13494+00 Rill erosion above blanket matting
- St#13496+00 Flow path of waterbar eroded
- St#13818+60 P1 half the height with sediment/possible slip

Recommended Corrective Action: Maintain all controls per the approved plan and specs.

Deadline: Within 24hr notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.


Inspector Signature:  Date: 3-28-19

FIELD INSPECTION PHOTO LOG


Project Name: Mountain Valley Pipeline

Date: Wednesday, March 20, 2019


- Fig. 1 St#13539+14 Slope lacks adequate stabilization

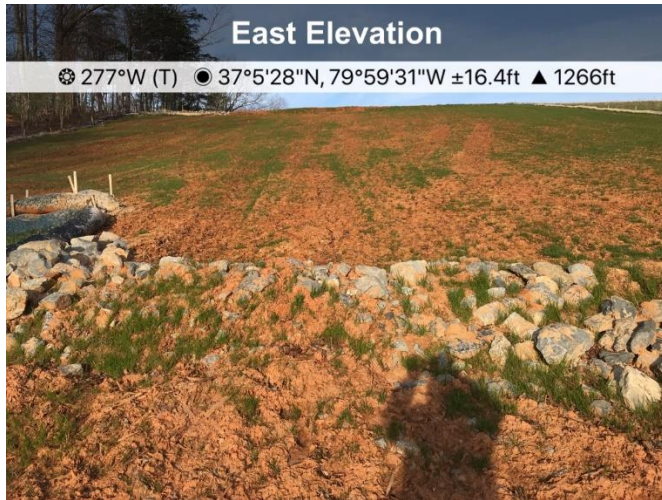

- Fig. 2 St#13533+52 Banks require repair and stabilization

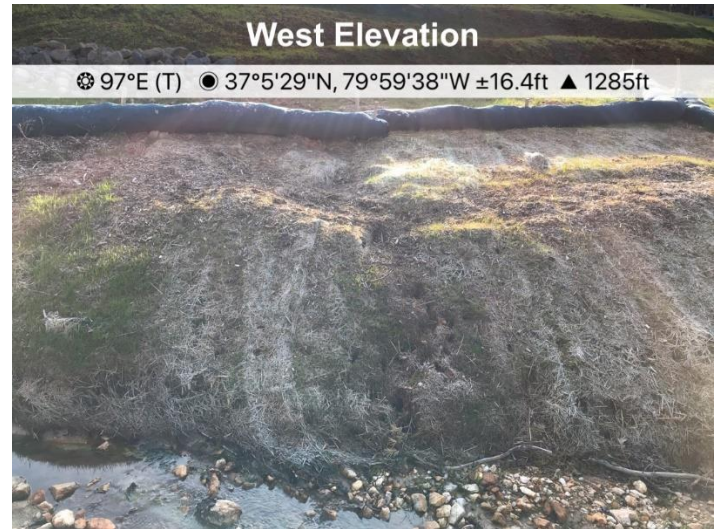

- Fig. 3 St#13528+00 Rills at farmer road crossing and CFS requires maintenance

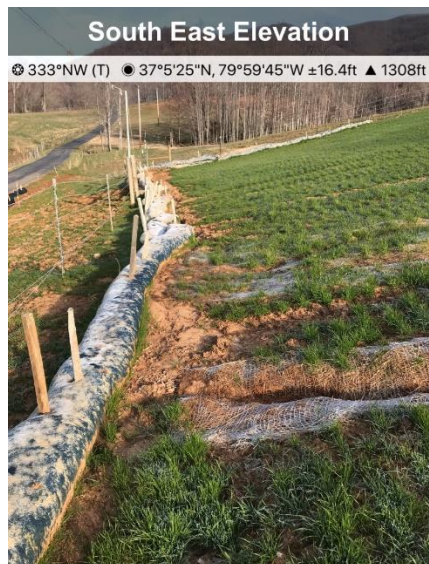

- Fig. 4 St#13500+00 Rill erosion along P1 SF and J-hook is overtopped



FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Wednesday, March 20, 2019

- Fig. 5 St#13494+00 Rill erosion above blanket matting



- Fig. 6 St#13496+00 Flow path of waterbar eroded



- Fig. 7 St#13818+60 P1 half the height with sediment/possible slip

