

FIELD INSPECTION

Project Name:	Mountain Valley Pipeline	Inspector:	Matthew Grant
Inspection Date:	Tuesday, March 5, 2019	Project Contact:	Brian Clauto
Spread: Pittsylvania County MP 299-300 St#15838-15865 MP285 St#15084- 15092 MP570 St#15055+88	Spread I	Weather (Wet/Dry/Rain):	Wet

STAGE OF CONSTRUCTION: (Check all that apply)

- ☐ Clearing

☐ Rough Grading

☐ Trench Excavation

☒ Pipe Assembly, Testing & Installation

☒ Backfilling and Grade Restoration

☐ Final Grading & Stabilization

☒ Other: Dormant

- | | | Yes | No | N/A |
|---|---|-------------------------------------|-------------------------------------|--------------------------|
| 1 | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | ☒ | ☐ | ☐ |
| 2 | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | ☐ | ☒ | ☐ |
| 3 | Areas of offsite sediment deposition were observed? | ☒ | ☐ | ☐ |

Comments:

- Streams / wetlands inspected included S-G2, W-G2, S-G9, S-D1-EPH.
- St#15850+56 stockpile lacks stabilization
- St#15865+00 level spreader lacks end cap
- St#15084+00 CWD has been breeched
- St#15086+00 CWD inlet has eroded
- St#15092+95 CFS waddle is torn
- St#15093+75 stockpile lacks stabilization
- St#15055+88 at S-D1-EPH stream bank has eroded from and sediment has entered the stream

Recommended Corrective Action: Maintain all controls per the approved plan and specs, remove sediment and stabilize per DEQ approval.

Deadline: Within 24hr notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.


Inspector Signature: Matthew Grant Date: 3-21-19

FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Tuesday, March 5, 2019

- Fig. 1 St#15850+56 stockpile lacks stabilization

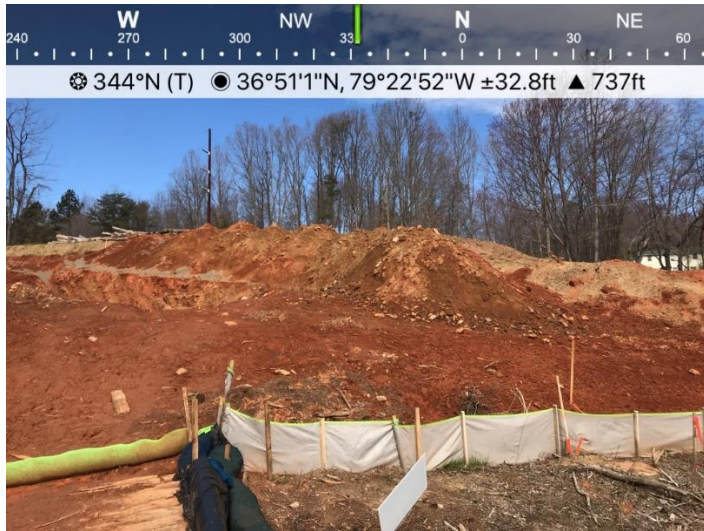

- Fig. 2 St#15865+00 level spreader lacks end cap



- Fig. 3 St#15084+00 CWD has been breached



- Fig. 4 St#15086+00 CWD inlet has eroded




FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Tuesday, March 5, 2019

- Fig. 5 St#15092+95 CFS waddle is torn

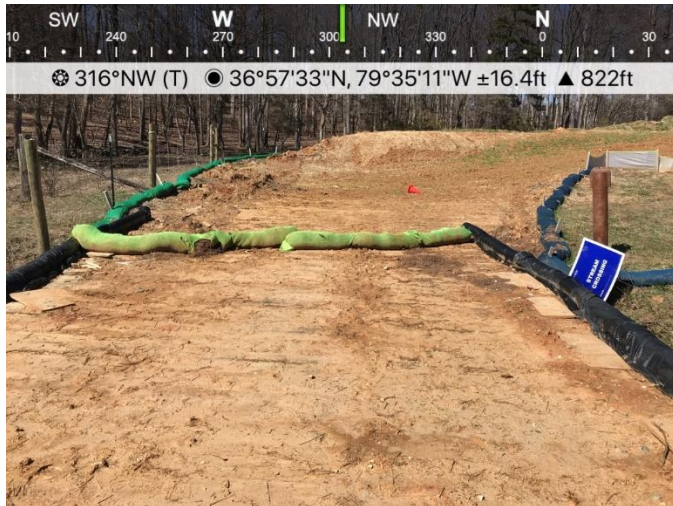

- Fig. 6 St#15093+75 stockpile lacks stabilization



- Fig. 7 St#15055+88 at S-D1-EPH stream bank has eroded from and sediment has entered the stream

